

8.8 MARCH 2021 FINANCIAL PERFORMANCE REPORT

File No:	Financial Reports
Author:	Coordinator Financial Services Business Performance Group
Attachments:	Att 1 - Monthly Financial Performance Report Att 2 - 2020-21 Capital Grant Funded Project Report March 2021

PURPOSE

To meet Council's legislative obligations, a monthly report is to be presented to Council on its financial performance and investments.

EXECUTIVE SUMMARY

This monthly financial performance report provides Council with a summary of performance against budget as at 31 March 2021 in terms of the operating result and delivery of the capital program.

Operating Performance

Table 1: Operating Budget as at 31 March 2021

	Original Budget \$000
Total Operating Revenue	465,069
Total Operating Expenses	460,733
Operating Result	4,336

Details of the monthly financial report are contained in Attachment 1.

OFFICER RECOMMENDATION

That Council receive and note the report titled "March 2021 Financial Performance Report".

FINANCE AND RESOURCING

This report sets out the details of Council's financial performance and investments for the month ending 31 March 2021 and meets Council's legislative reporting requirements.

CORPORATE PLAN

Corporate Plan Goal:	<i>An outstanding organisation</i>
Outcome:	5.7 - A financially sustainable organisation
Operational Activity:	5.7.1 - Develop and monitor Council's budget, including legislated requirements.

CONSULTATION

Portfolio Councillor Consultation

Consultation has been undertaken with the Portfolio Councillor, E Hungerford.

Internal Consultation

This report has been written in conjunction with advice from:

- Acting Group Executive Business Performance
- Acting Chief Financial Officer
- Acting Coordinator Financial Services

External Consultation

No external consultation is required for this report.

Community Engagement

No community engagement is required for this report.

Legal

This report ensures that Council complies with its legislative obligations with respect to financial reporting in accordance with Section 204 of the *Local Government Regulation 2012*.

Investment of funds is in accordance with the provisions of the *Statutory Bodies Financial Arrangements Act 1982* and the associated Regulations and the *Local Government Act 2009*.

Policy

Sunshine Coast Council's 2020/21 Investment Policy and
Sunshine Coast Council's 2020/21 Debt Policy.

Risk

Failure to achieve the budgeted operating result will negatively impact Council's capacity to complete its capital expenditure program.

Previous Council Resolution**Special Meeting Budget 25 June 2020 (SM20/16)**

That Council adopt Appendix A as tabled, pursuant to sections 169 and 170 of the Local Government Regulation 2012, Council's budget for 2020/21 financial year incorporating:

- i. *the statement of income and expenditure*
- ii. *the statement of financial position*
- iii. *the statements of changes in equity*
- iv. *the statement of cash flow*
- v. *the relevant measures of financial sustainability*
- vi. *the long term financial forecast*
- vii. *the Debt Policy (adopted by Council resolution on 11 June 2020)*
- viii. *the Revenue Policy (adopted by Council resolution on 11 June 2020)*
- ix. *the total value of the change, expressed as a percentage, in the rates and utility charges levied for the financial year compared with the rates and utility charges levied in the previous budget*
- x. *the Revenue Statement*
- xi. *Council's 2020/21 Capital Works Program, endorse the indicative four-year program for the period 2022 to 2025, and note the five-year program for the period 2026 to 2030*

- xii. the rates and charges to be levied for the 2020/21 financial year and other matters as detailed below in clauses 3 to 12 and*
- xiii. endorse the full time equivalent establishment as per the Sunshine Coast Council Establishment 2020/2021 report.*

Related Documentation

2020/21 Adopted Budget

Critical Dates

There are no critical dates for this report.

Implementation

There are no implementation details to include in this report.


Financial Performance Report

March 2021



Our region.
Healthy.
Smart.
Creative.

Statement of Income and Expenses March 2021

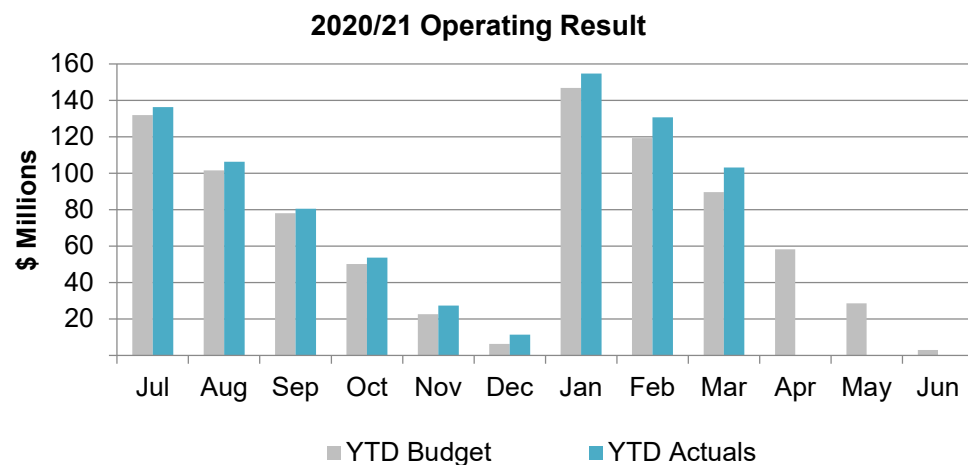

- Council has a positive operating result of \$98.4 million, which is \$8.6 million above the current budget as at 31 March 2021.




Statement of Income & Expenses

	Annual		YTD				Annual
	Original Budget \$000	Current Budget \$000	Current Budget \$000	Actuals \$000	Variance \$000	Variance %	Forecast Budget \$000
Operating Revenue							
Net Rates and Utility Charges	316,806	316,806	316,894	318,746	1,852	0.6%	316,806
Fees and Charges	57,125	56,309	44,380	48,645	4,265	9.6%	58,213
Interest Received from Investments	3,611	3,611	2,708	1,855	(853)	(31.5%)	3,611
Operating Grants and Subsidies	12,224	12,532	7,172	7,673	501	7.0%	13,332
Operating Contributions	287	287	260	158	(103)	(39.4%)	287
Unitywater Participation	49,838	49,838	32,778	32,778	0	0.0%	49,838
Other Revenue	21,040	20,877	15,277	15,792	514	3.4%	20,804
Internal Sales/Recoveries	4,138	4,138	2,948	1,862	(1,086)	(36.9%)	4,152
Total Operating Revenue	465,069	464,398	422,418	427,508	5,090	1.2%	467,043
Operating Expenses							
Employee Costs	147,973	148,358	110,139	110,015	(124)	(0.1%)	149,262
Materials and Services	184,678	184,996	127,156	122,806	(4,351)	(3.4%)	186,128
Finance Costs	12,080	12,080	9,107	9,108	1	0.0%	12,080
Company Contributions	1,554	1,554	1,554	1,562	8	0.5%	1,554
Depreciation Expense	88,276	88,276	66,229	66,231	1	0.0%	88,276
Other Expenses	22,255	22,505	15,477	15,799	322	2.1%	22,384
Recurrent Capital Expenses	3,917	3,917	3,025	3,632	608	20.1%	4,354
Total Operating Expenses	460,733	461,686	332,688	329,152	(3,536)	(1.1%)	464,039
Operating Result	4,336	2,712	89,730	98,356	8,626	9.6%	3,004
Capital Revenue							
Capital Grants and Subsidies	10,060	48,002	13,117	18,852	5,735	43.7%	48,932
Capital Contributions - Cash	31,599	31,599	23,811	39,258	15,447	64.9%	31,599
Capital Contributions - Fixed Assets	60,000	60,000	-	12,059	12,059	-	60,000
Total Capital Revenue	101,659	139,601	36,928	70,169	33,240	90.0%	140,531
Non-recurrent Expenses							
Profit/Loss on disposal, revaluation & impairment	-	-	-	418	418	-	-
Movements in landfill and quarry provisions	5,583	5,583	4,187	4,187	-	-	5,583
Assets Transferred to Third Parties	-	-	-	-	-	-	-
Total Non-recurrent Expenses	5,583	5,583	4,187	4,605	418	10.0%	5,583
Net Result	100,412	136,730	122,471	163,920	41,448	33.8%	137,952

Operating Result – March 2021

Operating Revenues

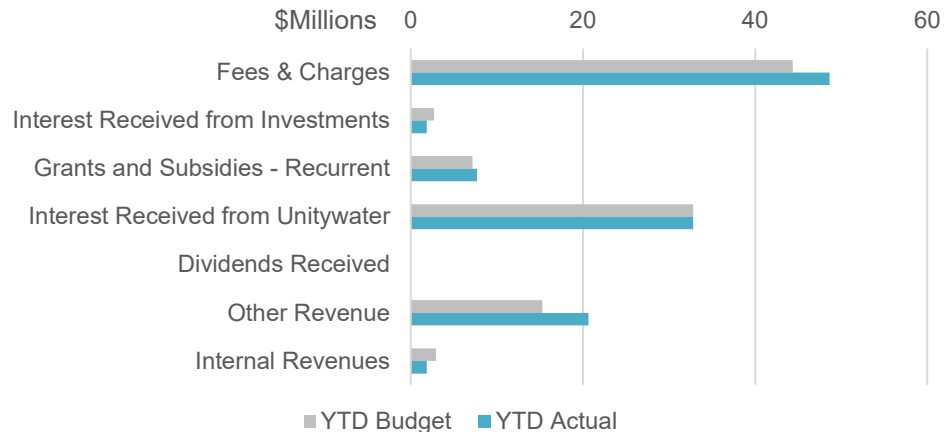

Substantial Revenue Variance for the Period Ending 31 March 2021

	Annual		YTD			
	Original Budget \$000	Current Budget \$000	Current Budget \$000	Actuals \$000	Variance \$000	Variance %
Net Rates and Utility Charges	316,806	316,806	320,446	322,225	1,779	0.6%
Fees and Charges	57,125	58,213	36,427	38,108	1,681	4.6%
Interest Received from Investments	3,611	3,611	2,107	1,476	(631)	(30.0%)
Operating Grants and Subsidies	12,224	12,532	7,172	7,673	501	7.0%
Other Revenue	21,040	20,805	13,171	13,625	454	3.4%
Internal Sales/Recoveries	4,138	4,124	2,230	1,390	(841)	(37.7%)

Operating Summary


	Annual		YTD			
	Original Budget \$000s	Current Budget \$000s	Current Budget \$000s	Actuals \$000s	Variance \$000s	Variance %
Operating Revenue	465,069	464,398	422,418	427,508	5,090	1.2%
Operating Expenses	456,816	457,769	329,663	325,520	(4,144)	(1.3%)
Recurrent Capital Expenses	3,917	3,917	3,025	3,632	608	20.1%
Operating Result	4,336	2,712	89,730	98,356	8,626	9.6%
Capital Revenue	101,659	139,601	36,928	70,169	33,240	90.0%
Non-recurrent Expenses	5,583	5,583	4,187	4,605	418	10.0%
Net Result	100,412	136,730	122,471	163,920	41,449	33.8%

As at 31 March 2021 \$427.5 million operating revenue had been achieved which is \$5.1 million more than current budget for the same period.

- This is largely due to:
 - Net Rates and Utility Charges** – An increase in waste collection services has led to a 2.7% increase in cleansing charges on 2019/20 result and higher than the increase in service level anticipated in the 2020/21 budget.
 - Fees and Charges** – Fees relating to Council's Caravan Parks are currently \$2.1m above budget. Tip Fees and Development Services Fees are also above budget by \$2.1m and \$1.1m.
 - Interest Received from Investments** - The reduced RBA cash rate has had an impact on Council's investment revenue.
 - Operating Grants and Subsidies** – Council has received unbudgeted grant funds for the Qld Bushfire Local Economy Recovery Grant program of \$400,000.
 - Other Revenue** – The positive variance in Other revenue is due to \$108,000 in the recoupment of legal fees, \$124,000 received in sponsorship for the Horizon festival and the sale of recyclables being \$209,000 above budget.
 - Internal Sales** – Internal Quarry Sales are currently below budget by \$1.3m

Operating Result – March 2021 (continued)

Operating Expenses

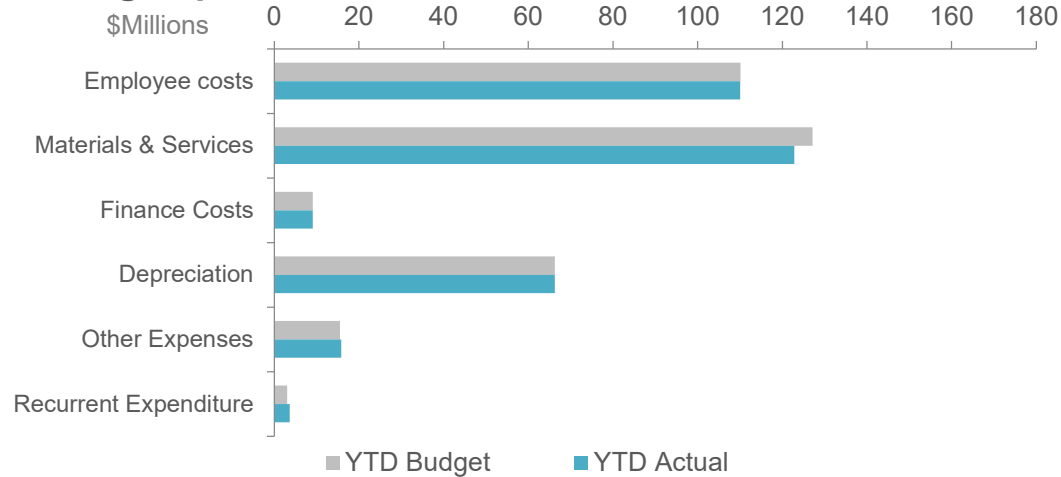

Operating Summary

	Annual		YTD			
	Original Budget \$000s	Current Budget \$000s	Current Budget \$000s	Actuals \$000s	Variance \$000s	Variance %
Operating Revenue	465,069	464,398	422,418	427,508	5,090	1.2%
Operating Expenses	456,816	457,769	329,663	325,520	(4,144)	(1.3%)
Recurrent Capital Expenses	3,917	3,917	3,025	3,632	608	20.1%
Operating Result	4,336	2,712	89,730	98,356	8,626	9.6%
Capital Revenue	101,659	139,601	36,928	70,169	33,240	90.0%
Non-recurrent Expenses	5,583	5,583	4,187	4,605	418	10.0%
Net Result	100,412	136,730	122,471	163,920	41,449	33.8%

As at 31 March 2021 \$326 million of the \$330 million budget year to date had been expended which resulted in an underspend of 4.1 million or 1.3%

Materials and Services:


- Across whole of Council there has been savings below budget in corporate costs of fuel \$564,000, electricity \$242,000 and water and sewerage \$585,000.
- The reduction in revenue for the Quarry has resulted in reduced associated material costs of \$884,000. Similarly the reduction in fees and charges revenue for Response Services has resulted in a \$365,000 underspend.
- Transport Levy Projects are underspent by \$215,000 due to the timing in the delivery of road maintenance and Cultural Heritage Contracts are currently \$289,000 underspent.

Substantial Expenditure Variance for the Period Ending 31 March 2021

	Annual		YTD			
	Original Budget \$000	Current Budget \$000	Current Budget \$000	Actuals \$000	Variance \$000	Variance %
Materials and Services	184,678	184,996	127,156	122,806	(4,351)	(3.4%)

Capital Expenditure – March 2021

SCC Base Capital Expenditure

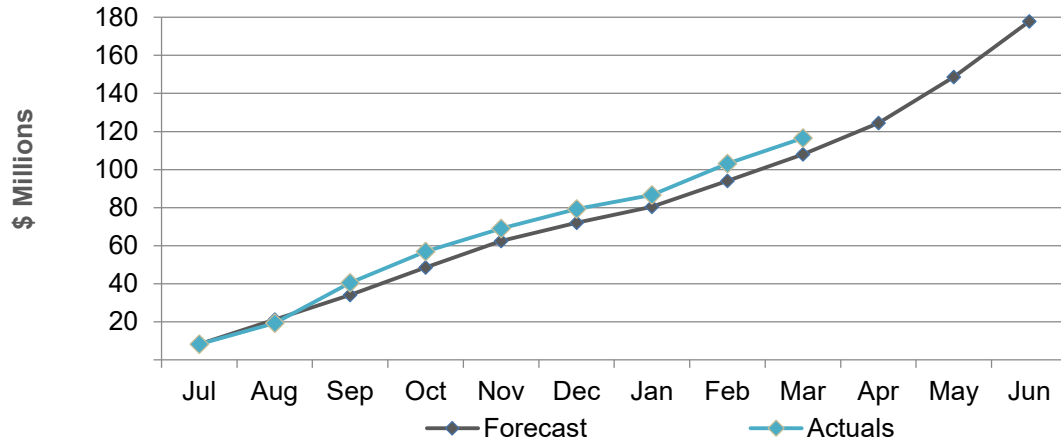


- As at 31 March 2021 \$176.7 million of Council's \$287.3 million Capital Works Program was financially expended.
- The Core Capital Program has progressed 56.9% of budget, an actual spend of \$102 million.
- Corporate Major Projects progressed 85.4% and The Sunshine Coast Airport Runway Project progressed 80% of their respective annual budgets.



Capital Expenditure				March 2021		
	Annual		YTD		Year End	
	Original Budget \$000s	Current Budget \$000s	Actuals \$000s	% of FY Budget Spent	Forecast Year End Actual	Forecast Year End Variance to Budget
Aerodromes	350	250	147	58.8%	233	(17)
Buildings and Facilities	45,717	38,395	16,066	41.8%	27,945	(10,450)
Coast and Canals	2,830	3,458	3,459	100.0%	3,639	181
Environmental Assets	1,375	3,195	1,296	40.6%	2,944	(251)
Fleet	2,000	2,037	1,434	70.4%	1,878	(159)
Holiday Parks	1,255	992	789	79.5%	1,153	161
Information Technology	6,275	7,579	3,850	50.8%	6,489	(1,090)
Parks and Gardens	15,141	19,025	11,210	58.9%	19,844	819
Quarries	480	480	268	55.9%	377	(103)
Stormwater	6,772	6,601	2,752	41.7%	6,384	(217)
Transportation	65,588	83,030	53,444	64.4%	81,759	(1,271)
Waste	14,723	13,683	7,060	51.6%	9,696	(3,987)
Total SCC Core Capital Program	162,506	178,725	101,776	56.9%	162,341	(16,383)
Minor Works	4,620	4,921	694	14.1%	2,377	(2,544)
Corporate Major Projects	16,733	18,375	15,687	85.4%	17,510	(865)
Strategic Land and Commercial Properties	9,949	26,788	14,745	55.0%	25,222	(1,565)
Maroochydore City Centre	11,879	14,156	8,363	59.1%	9,842	(4,314)
Submarine Cable IBN	-	-	3	-	3	3
Sunshine Coast Airport Runway	36,718	44,288	35,447	80.0%	44,430	142
Total Other Capital Program	79,899	108,528	74,939	69.1%	99,384	(9,143)
TOTAL	242,405	287,252	176,714	61.5%	261,726	(25,526)
The above program of works includes recurrent and non-recurrent expenditure, as reporting in the operating statement						
Recurrent Expenses			3,632	-		
Non-Recurrent Expenses			4,605	-		

Capital Expenditure – March 2021 (continued)

SCC Core % YTD spent compared to profiled budget by

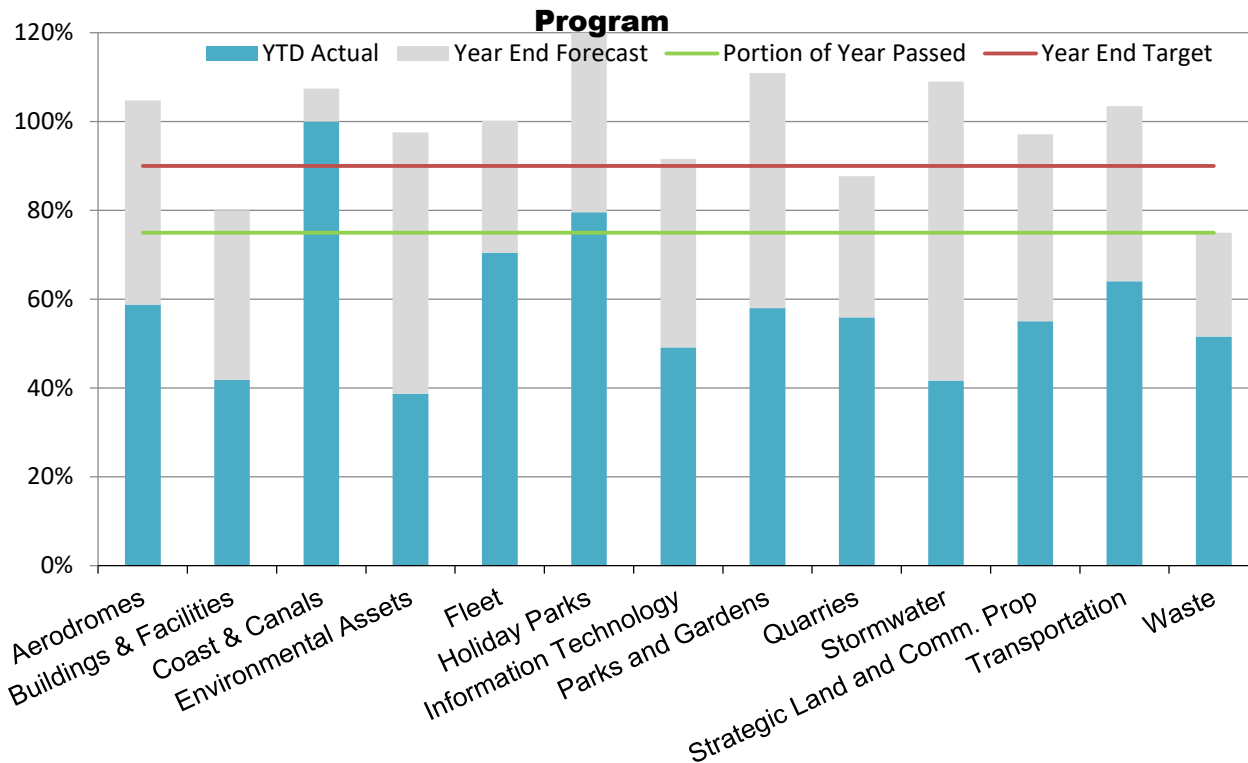

Aerodromes

- Delivery of the runway lighting replacement project for Caloundra Aerodrome is currently underway and scheduled for completion in May 2021.

Buildings and Facilities

- The Sunshine Coast City Hall commenced construction in late August 2020. A portion of the current financial year budget will be deferred into next financial year to align with the expected contract payment cash flows. The construction program remains on track for complete June 2022.

Environmental Assets

- Design of the \$1.3 million State Government funded trails hub at Sugar Bag Road has been finalised. Construction is currently underway with an anticipated completion in June 2021.

Information Technology

- Several projects in the Information Technology Program will be deferred due to shortage in resources.

Parks and Gardens

- The contract has been awarded for the design and construction of the new State Funded clubhouse and change rooms at the Palmwoods cricket club.

Stormwater

- The \$1.2 million relining of damaged stormwater pipe program is currently 50% complete.

Strategic Land and Commercial Properties

- Several land acquisitions relating to transport corridors will be deferred due to delays in land settlements.

Transport



- Planned spend forecasted from February to June for Federal grant funded stimulus projects within the Pedestrian and Cyclist Enabling Facilities, Gravel and Sealed Road Network sub-programs.
- Council's \$19.6 million Road Resurfacing and Rehabilitation program has progressed 66% completion in March. Alongside the reseal program, the \$2.4 million bus stop replacement and installation program has progressed 78%.

Waste

- An extended timeframe for the evaluation of tenders for the new Materials Recycling Facility in will result in deferral of funds to next financial year.

Cash Flows and Balance Sheet

Cash Balance

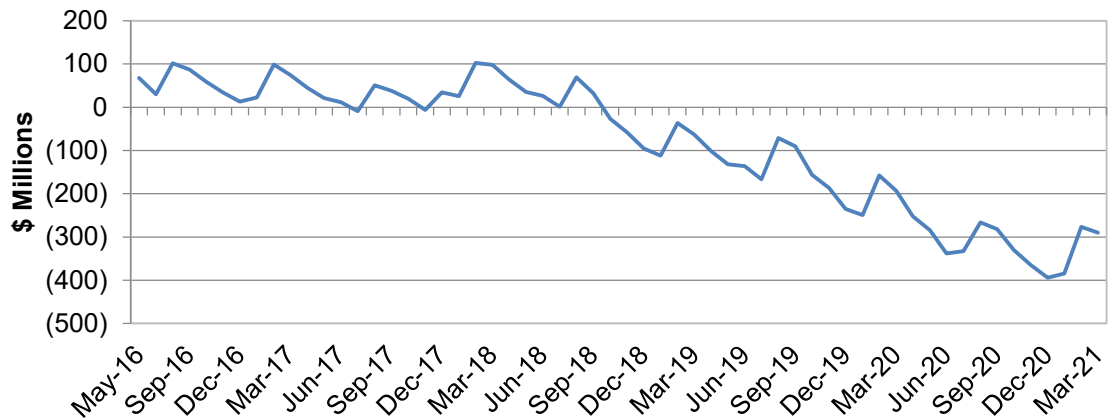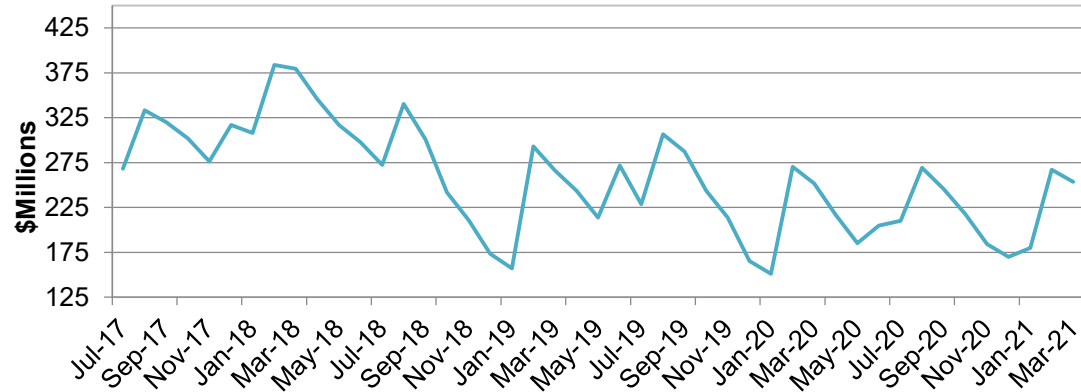


Cash and Balance Sheet - March 2021

	Original Budget \$000s	Current Budget \$000s
CASH FLOWS		
Opening Cash	229,139	197,632
Net Cash Inflow/(Outflows) from:		
Operating Activities	48,942	42,253
Investing Activities	(149,603)	(145,196)
Financing Activities	90,433	98,104
Net Increase/(decrease) in Cash Held	(10,229)	(4,839)
Cash at year end	218,910	192,793
BALANCE SHEET		
Current Assets	272,962	246,571
Non Current Assets	6,173,956	6,174,143
Total Assets	6,446,918	6,420,714
Current Liabilities	408,307	397,781
Non Current Liabilities	410,419	422,676
Total Liabilities	818,726	820,457
Net Community Assets/Total Community Equity	5,628,192	5,600,257

- Council's cash at 31 March 2021 is \$242 million excluding trust accounts
- Council's debt at 31 March 2021 is \$543 million

Debt

Debt Balance

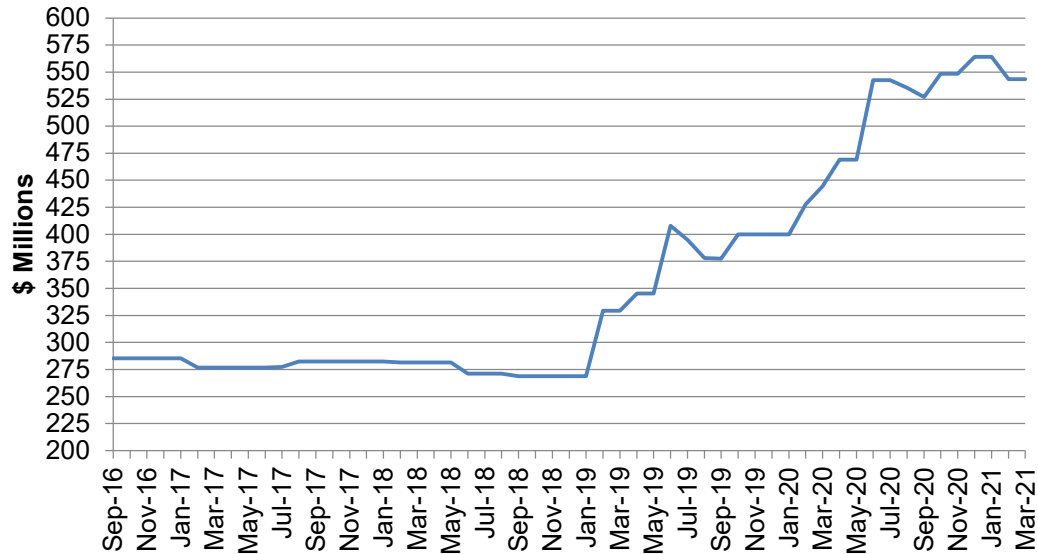

Sunshine Coast Council’s debt program is governed by the 2020/21 Debt Policy, which was adopted with the Original Budget adoption on 25 June 2020. The Debt policy was revised during Budget Review 2 and adopted by Council at the December Ordinary meeting. New borrowings are undertaken in accordance with the Queensland Treasury Corporation Guidelines, the Statutory Bodies Financial Arrangements Act 1982 and Section 192 of the Local Government Regulation 2012.

The below table contains Sunshine Coast Council's adopted debt balance for 2020/21

Debt - 2020/21

	Opening Balance	Debt Redemptions	New Borrowings	Closing Balance
	\$000	\$000	\$000	\$000
Sunshine Coast Council Core	190,864	12,292	58,975	237,547
Sunshine Coast Airport Expansion Project	211,492	-	57,430	268,922
Maroochydore City Centre	132,530	8,847	7,500	131,183
Sunshine Coast International Broadband Network	11,236	908	-	10,328



Our region.
Healthy.
Smart.
Creative.



List of Approved Capital Works Projects Including Grant Funding from State and Federal Government

	Description	Division	Suburb	Estimated Construction Start Month	Construction Completed Month	TOTAL Grant Revenue \$'000	Project Expenditure to date \$'000
Federal Government						(\$22,309)	\$3,330
Local Road and Community Infrastructure Grant Funding - Round 1						(\$3,650)	\$1,237
1	H3798 - LRCI Eastern Mary River Road Raddatz Bridge	Division 05	Cambroon	January 2021	May 2021	(\$670)	\$250
2	H4287 - LRCIP Glenview Road Upgrade Stage 4	Division 05	Glenview	February 2021	May 2021	(\$800)	\$477
3	H5121 - LRCIP Cottonwood Street Mudjimba - Pathway	Division 08	Mudjimba	June 2021	June 2021	(\$53)	\$0
4	H9403 - LRCIP Alfriston Drive Buderim - Pathway	Division 06	Buderim	November 2020	December 2020	(\$180)	\$179
5	H9509 - LRCIP Ghost Gum Ave Kuluin - Pathway	Division 07	Kuluin	February 2021	March 2021	(\$75)	\$35
6	H9836 - LRCIP Camp Flat Road - Section 5 - Widening	Division 09	Bli Bli	February 2021	June 2021	(\$1,450)	\$231
7	H9845 - LRCIP Carmel Street Golden Beach - Pathway	Division 02	Golden Beach	June 2021	July 2021	(\$36)	\$40
8	K1486 - LRCIP Ridgehaven Court - Pathway Construction	Division 03	Aroona	June 2021	June 2021	(\$63)	\$0
9	H9848 - LRCIP Laneway between Neerim Dr - Brisbane	Division 04	Mooloolaba	February 2021	March 2021	(\$29)	\$0
10	H9849 - LRCIP Hinley Ave and Gibson Street Maroochydore	Division 08	Maroochydore	May 2021	May 2021	(\$154)	\$0
11	H9850 - LRCIP Stringybark Rd - Pathway	Division 07	Buderim	April 2021	April 2021	(\$67)	\$22
12	H9851 - LRCIP Scrub Rd Coolum Beach - Pathway	Division 09	Coolum Beach	March 2021	March 2021	(\$73)	\$3
Blackspot Funding						(\$3,555)	\$761
13	H8463 - BlackSpot Glenview Road Hazard Removal	Division 05	Glenview	October 2020	May 2021	(\$385)	\$194
14	H8464 - BlackSpot Petrie Creek Rd Alignment Warning	Division 07	Rosemount	July 2020	November 2020	(\$240)	\$102
15	H8465 - BlackSpot Tunnel Ridge Road Hazard Removal	Division 01	Mooloolah Valley	January 2021	June 2021	(\$785)	\$121
16	H8466 - BlackSpot Lindsay Road Alignment Warning	Division 07	Buderim	November 2020	April 2021	(\$445)	\$14
17	H8467 - BlackSpot Hunchy Road Curve Widening	Division 05	Hunchy	February 2021	July 2021	(\$1,700)	\$331
Local Road and Community Infrastructure Grant Funding - Round 2						(\$11,069)	\$399
18	H3790 - LRCIP2 - Citrus Road Gravel Road Upgrade	Division 05	Palmwoods	July 2021	December 2021	(\$2,200)	\$30
19	H3799 - LRCIP2 - Zgrajewski Rd Gravel Rd Upgrade	Division 09	Yandina Creek	July 2021	December 2021	(\$3,200)	\$15
20	H3800 - LRCIP2 - Cupania Street East S2 Kerb and Channel	Division 08	Mudjimba	August 2021	August 2021	(\$890)	\$3
21	H3941 - LRCIP2 - Crosby Hill Road Pathway WOR	Division 07	Buderim	May 2021	September 2021	(\$809)	\$23
22	H4223 - LRCIP2 - Scholars Drive to Columbia Street	Division 06	Sippy Downs	June 2021	December 2021	(\$500)	\$2
23	H4592 - LRCIP2 - Lees Road Western Section Gravel Road Upgrade	Division 10	Bridges	September 2021	November 2021	(\$650)	\$54
24	H9360 - LRCIP2 - Railway Street Service Road	Division 01	Landsborough	June 2021	August 2021	(\$130)	\$11
25	K1050 - LRCIP2 - Cromwell St Battery Hill - Path	Division 02	Battery Hill	April 2021	May 2021	(\$85)	\$0
26	K1051 - LRCIP2 - Enfield Crescent Battery Hill	Division 02	Battery Hill	April 2021	June 2021	(\$55)	\$0
27	K1451 - LRCIP2 - Coastal Pathway - Bokarina Warana	Division 03	Warana	March 2021	May 2021	(\$200)	\$247
28	K1484 - LRCIP2 - Meridan Way Lighting	Division 03	Meridan Plains	June 2021	September 2021	(\$350)	\$14
29	K1492 - LRCIP2 - Spray Seal - Old Gympie Road Resurfacing	Division 01	Glasshouse Mountains	November 2021	November 2021	(\$168)	\$0
30	K1493 - LRCIP2 - Spray Seal - Bald Knob Road	Division 01	Peachester	November 2021	November 2021	(\$186)	\$0
31	K1494 - LRCIP2 - Rehab King Road	Division 05	Mooloolah Valley	February 2021	March 2021	(\$534)	\$0
32	K1495 - LRCIP2 - Asphalt Mountain View Road	Division 05	Maleny	October 2021	October 2021	(\$462)	\$0
33	K1496 - LRCIP2 - Bunya Road 2	Division 10	Bridges	April 2021	May 2021	(\$649)	\$0
Community Sport Infrastructure Grant Program						(\$181)	\$360
34	H8672 - Maroochydore Rugby Union Change Room	Division 04	Maroochydore	February 2020	December 2020	(\$181)	\$360
35 Roads to Recovery Program						(\$3,654)	
National Stronger Regions Fund						(\$200)	\$571
36	B3798 - Howard Street Tram Project	Division 10	Nambour		February 2021	(\$200)	\$571

List of Approved Capital Works Projects Including Grant Funding from State and Federal Government

	Description	Division	Suburb	Estimated Construction Start Month	Construction Completed Month	TOTAL Grant Revenue \$'000	Project Expenditure to date \$'000
State Government						(\$32,910)	\$9,357
2021 COVID Works for Queensland						(\$5,350)	\$2,844
37	H8752 - Caloundra Reserve 1000 AFL Little Athletics	Division 02	Golden Beach	August 2020	September 2020	(\$60)	\$127
38	H9769 - Palmwoods Cricket AFL Clubhouse Upgrade	Division 05	Palmwoods	October 2020	April 2021	(\$500)	\$240
39	H9771 - Coolum Tennis Court Renewal	Division 09	Coolum Beach	October 2020	February 2021	(\$350)	\$472
40	H9774 - Sunshine Coast Hockey synthetic field resurface	Division 07	Buderim	October 2020	December 2020	(\$450)	\$489
41	H9776 - Yandina Cricket Clubhouse Upgrade	Division 10	Yandina	March 2021	June 2021	(\$500)	\$100
42	H9777 - Skippy Park Oval Drainage	Division 01	Beerwah	March 2021	June 2021	(\$250)	\$11
43	H9778 - Meridan Fields Bollards	Division 03	Meridan Plains	September 2020	October 2020	(\$25)	\$26
44	H9779 - North Shore Multi-Sports Complex storage	Division 08	Pacific Paradise	January 2021	March 2021	(\$100)	\$84
45	H9780 - Buderim Wanderers Football Club field lighting	Division 07	Buderim	November 2020	January 2021	(\$120)	\$95
46	H9784 - Maroochydore Multi-Sports Field Lighting	Division 07	Maroochydore	July 2020	October 2020	(\$425)	\$436
47	H9786 - Maleny Showgrounds solar installation	Division 05	Maleny	December 2020	February 2021	(\$200)	\$228
48	H9810 - Sugar Bag Road - Trails Hub	Division 02	Little Mountain	January 2021	May 2021	(\$1,320)	\$280
49	H9814 - Nambour Aquatic Centre Water Slide development	Division 10	Nambour	March 2021	July 2021	(\$1,050)	\$257
School Transport Infrastructure Program						(\$2,360)	\$1,407
50	H9274 - STIP Windsor Road Burnside Supervised Crossing and Path	Division 10	Burnside	October 2020	October 2020	\$0	\$193
51	H9276 - STIP Blaxland Road Burnside New Pathway	Division 10	Burnside	June 2021	June 2021	\$0	\$53
52	H9277 - STIP Windsor Road Burnside Nambour Special School Bus Parking Area	Division 10	Burnside	February 2021	June 2021	\$0	\$19
53	H9278 - STIP Glenview Rd Glenview State School Stop-Drop-Go Parking	Division 05	Glenview	October 2020	October 2020	\$0	\$105
54	H9279 - STIP Havana Road East Coolum High Parking	Division 09	Coolum Beach	November 2020	March 2021	\$0	\$810
55	H9281 - STIP Lady Musgrave Drive Mountain Creek	Division 06	Mountain Creek	October 2020	November 2020	\$0	\$51
56	H9282 - STIP Pacific Bvd Buddina Pedestrian	Division 04	Buddina	November 2020	November 2020	\$0	\$69
57	H9283 - STIP Main Street Buderim Shared Path Buderim Mountain State School	Division 07	Buderim	February 2021	February 2021	\$0	\$107
58	H9460 - STIP School Transport Infrastructure Program	Division 20	Whole of Region	Not Applicable	Not Applicable	(\$2,360)	\$0
Queensland Transport and Roads Investment Program						(\$4,000)	\$2,241
59	H3747 - Mooloolaba Transport Corridor - D and C	Division 04	Mooloolaba		November 2023	(\$4,000)	\$2,241
Unite and Recover Stimulus Package						(\$6,500)	\$2,060
60	B4741 - Place Making Mooloolaba Master Plan	Division 04	Mooloolaba	February 2021	August 2021	(\$4,500)	\$1,298
61	H9821 - Albany Lakes Park Sippy Downs Play Space	Division 06	Sippy Downs	April 2021	July 2021	(\$150)	\$114
62	H9880 - Grahame Stewart Park Change Facilities	Division 03	Currimundi	September 2020	January 2021	(\$200)	\$203
63	H9895 - Beerwah Community Meeting Place	Division 01	Beerwah	February 2021	June 2021	(\$1,650)	\$446
Cycle Network Local Government Grants Program 2020-2021						(\$660)	\$112
64	H4730 - Seib Road Eumundi - Pedestrian Bridge	Division 10	Eumundi	May 2021	September 2021	(\$502)	\$34
65	H7509 - Alex Bluff Foreshore Coastal Pathway - forward design	Division 04	Alexandra Headland	April 2021	June 2021	(\$50)	\$41
66	H7862 - LGIP Active Transport Concept Planning	Division 20	Whole of Region	Not Applicable	Not Applicable	(\$38)	\$4
67	H7903 - Petrie Creek Road Cycle Lanes	Division 07	Rosemount	May 2021	May 2021	(\$70)	\$33
Cycle Network Program						(\$330)	\$692
68	H1583 - Bradman Ave Chambers Island to Pic Point	Division 08	Maroochydore	April 2020	September 2020	(\$225)	\$684
69	H4857 - LGIP Bundilla Bvd Cycle Lanes	Division 06	Mountain Creek	TBA	TBA	(\$105)	\$8
70 Bus Stop Shelter Program						(\$696)	
71 Passenger Transport Accessible Infrastructure Program						(\$515)	
72 Jobs and Regional Growth Fund Assistance						(\$12,500)	

Notes:

- Grant funds to be received over 2020/21 and 2021/22 Financial Year.
